DENTON INDEPENDENT SCHOOL DISTRICT EMPOWERING LIFE-LONG LEARNERS

Construction, Planning & Growth

Construction Report

March 2025

Active Construction Timeline



| Facility | Phase of Development | Move In Date | |
|---|-------------------------|--------------|--|
| Hill Elementary School | Under Construction | TBD | |
| Reeves Elementary School | Under Construction | Summer 2025 | |
| Denton High School Multipurpose | Under Construction | Fall 2025 | |
| Braswell High School Multipurpose & Additions | Under Construction | 2025 | |
| Guyer High School Multipurpose & Ag Facility | Under Construction | 2025 | |
| Ryan High Renovation & Multipurpose | Under Construction | 2026 | |
| High School #5 | Under Construction | 2027 | |
| Harpool Middle School Track & Field | Under Construction | 2025 | |
| Navo Middle School Track & Field | Under Construction | 2025 | |
| Strickland Middle School Track & Field | Under Construction | 2025 | |

Active Project Timeline



| Facility | Phase of Development | Construction Commencing | Move In Date |
|--|-------------------------|-------------------------|--------------|
| Borman Elementary School Replacement | Awaiting Permit | Spring 2025 | August 2026 |
| W.S. Ryan Elementary School Renovation | Awaiting Permit | Summer 2025 | August 2025 |
| Hodge Elementary School Renovation | Awaiting Permit | Summer 2025 | August 2025 |
| C.H. Collins Facility Upgrades | Awaiting Permit | Summer 2025 | August 2025 |
| Crownover Middle School Facility Upgrades | Awaiting Permit | Summer 2025 | August 2025 |
| Harpool Middle School Facility Upgrades | Awaiting Permit | Summer 2025 | August 2025 |
| McMath Middle School Facility Upgrades | Awaiting Permit | Summer 2025 | August 2025 |
| Providence Elementary School Facility Upgrades | Awaiting Permit | Summer 2025 | August 2025 |
| Stephens Elementary School Facility Upgrades | Awaiting Permit | Summer 2025 | August 2025 |
| E.P. Rayzor Roofing | Awaiting Permit | Summer 2025 | August 2025 |
| Stephens Administration Roofing | Awaiting Permit | Summer 2025 | August 2025 |



DENTON INDEPENDENT SCHOOL DISTRICT EMPOWERING LIFE-LONG LEARNERS

Construction, Planning & Growth


Borman Elementary School

March 2025

Borman Elementary School



2023 Bond Authorization
Architects – Corgan
Contractor – Joeris
Move In – Summer 2026

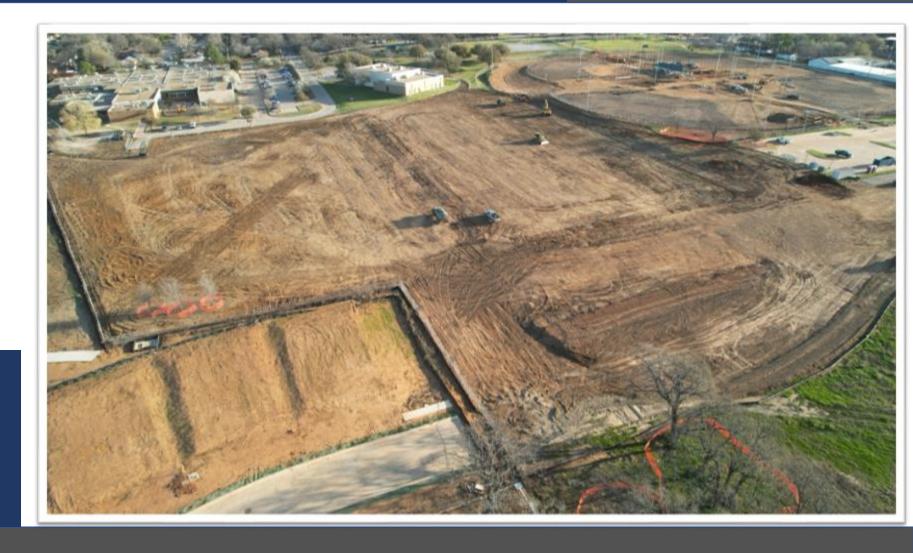

Borman Elementary School



2023 Bond Authorization
Architects – Corgan
Contractor – Joeris
Move In – Summer 2026

Upcoming tasks:

- Grading of site to begin
- Building pad to begin mid April
- Site utilities to begin mid April
- Piers and grade beams to begin mid May



DENTON INDEPENDENT SCHOOL DISTRICT EMPOWERING LIFE-LONG LEARNERS

Construction, Planning & Growth

High School #5

March 2025







2023 Bond Authorization
Architects – VLK Architects
Contractor – CORE
Move In – 2027

Tasks completed previous 90 days:

- Site clearing and grading
- Construction trailers, laydown yard and site fencing
- Underground utilities began
- Installing geothermal wells
- Constructing building pads

Upcoming tasks:

- Rough grading to be completed
- Continue underground utilities
- Continue geothermal wells
- Construct building piers and grade beams
- Install fire lanes around building pad
- Concrete foundation and slab























DENTON INDEPENDENT SCHOOL DISTRICT EMPOWERING LIFE-LONG LEARNERS

Construction, Planning & Growth

Reeves Elementary School

March 2025



2023 Bond Authorization
Architects – Pfluger
Contractor – Balfour Beatty
Move In – Summer 2025







2023 Bond Authorization
Architects – Pfluger
Contractor – Balfour Beatty
Move In – Summer 2025

Tasks Previous 90 Days:

- Steel detailing and decking
- Brick installation at Gym
- Slab on metal deck in multiple areas
 to be completed
- Punch Windows
- Exterior Framing and Sheathing ongoing
- Storefronts and curtain walls will begin

Upcoming Tasks:

- Construction of Riney Road to begin
- Brick veneer to be completed
- Canopy columns being installed
- Interior finishes ongoing
- Millwork ongoing
- Mechanical/Electrical/Plumbing overhead ongoing




2023 Bond Authorization
Architects – Pfluger
Contractor – Balfour Beatty
Move In – Summer 2025







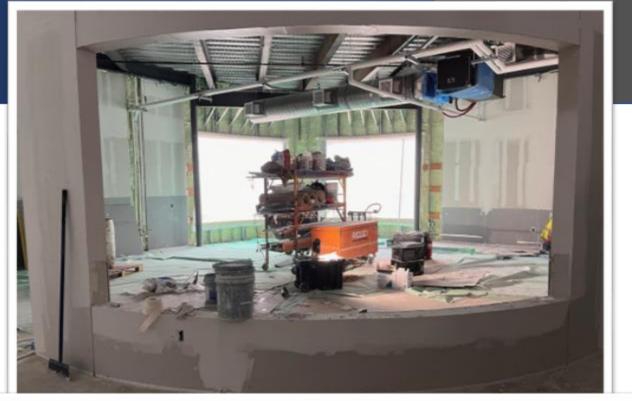





2023 Bond Authorization
Architects – Pfluger
Contractor – Balfour Beatty
Move In – Summer 2025







2023 Bond Authorization
Architects – Pfluger
Contractor – Balfour Beatty
Move In – Summer 2025



DENTON INDEPENDENT SCHOOL DISTRICT EMPOWERING LIFE-LONG LEARNERS

Construction, Planning & Growth

Braswell High School Multipurpose Facility

March 2025









2023 Bond Authorization
Architects – VLK
Contractor – Balfour Beatty
Move In – 2025

Tasks Previous 90 Days:

- Prep of fire lanes ongoing
- Grade beams and piers ongoing
- Slab on grade to begin
- Erecting steel for indoor facility completed
- Batting cages for Baseball/Softball completed

Upcoming Tasks:

- Mechanical/Electric/Plumbing ongoing
- Sheathing on east side to begin
- Batting cages CMU and steel
- Construction of outdoor practice field ongoing
- Construction of discus area starting














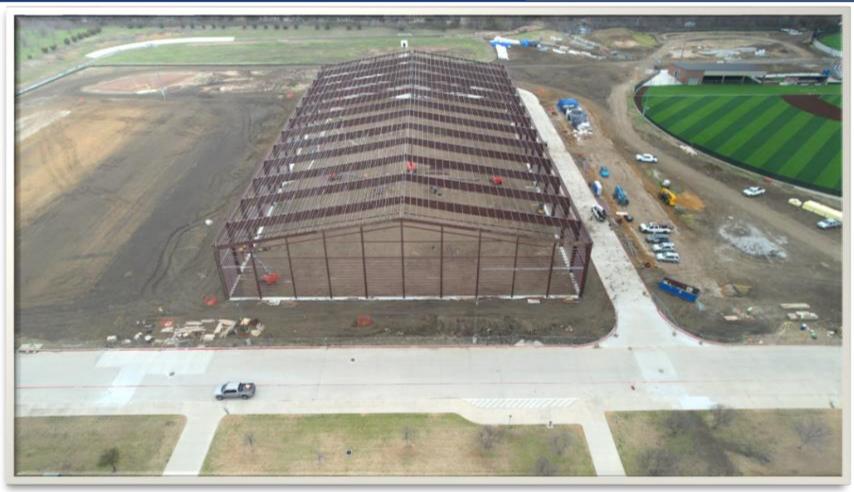



Questions?

Prepared by:

Brandon Boyter Executive Director of Construction, Planning & Growth
