

TECHNOLOGY UPDATE

Select Active Bond Projects by Department

Network Infrastructure

New Construction Fiber Infrastructure

Martinez—Complete 5/17

Hill—Northern path has conflict. Re-engaging option B build to 720.

Campus Infrastructure

New Calhoun—Complete


Martinez—Planned installation moving from 5/20 to mid June.

Hill—End of May expectation wired/wireless.

Evers—Expenses encumbered. Coordination with Construction Renovation efforts prior to start of school.

VOIP Gateway

Design and Planning for District-wide equity for VoIP survivability

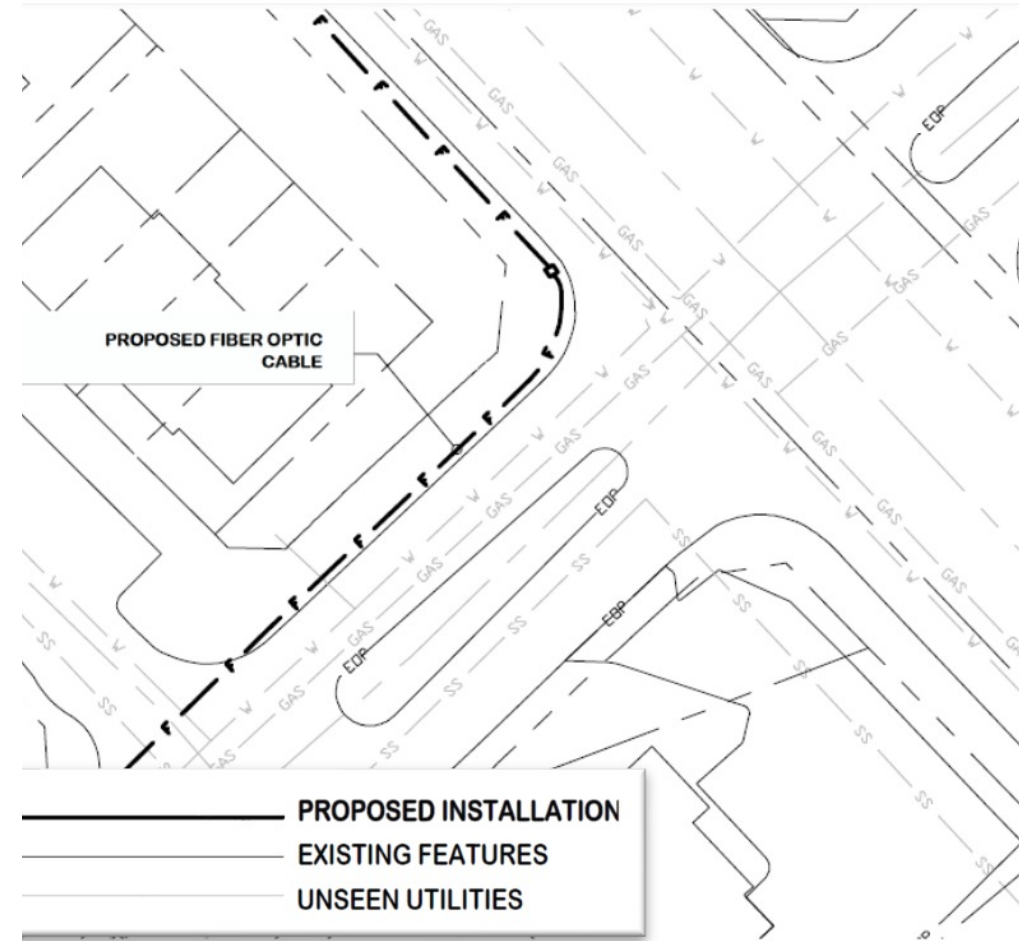



Systems Infrastructure

Cybersecurity

Hyper-V to UCS-X/VMWare Migration

- 70% complete currently
- 100% complete by July 1, 2024

Technology Services

Expo Standard Updated

- All Elementary classrooms received 3D Dremel printers as part of their new standard

BHS Commons and Competition Gym A/V

- Absen Video Wall - commons
- New Sound Rack, Amps and Speakers – Atlas & Extron – both spaces
- New Control Panel – Extron TouchLink Pro – both spaces
- Microphones – Shure – both spaces

Nelson and Houston Café and Gym A/V Upgrade Completed

