

DENTON INDEPENDENT SCHOOL DISTRICT EMPOWERING LIFE-LONG LEARNERS

Construction, Planning & Growth

Construction Report

November 2025

Active Construction Timeline



Facility	Phase of Development	Move In Date
Braswell High School Multipurpose & Additions	In Progress	December 2025
Guyer High School Multipurpose & Ag Facility	In Progress	February 2026
Ryan High Renovation & Multipurpose	In Progress	2026
High School #5	In Progress	Opening 2028
Borman Elementary School Replacement	In Progress	Opening 2026
Ginnings Elementary Rebuild	In Progress	TBD

Future Project Timeline



Facility	Phase of Development	Move In Date
Houston Elementary School Renovation	Awaiting Board Approval	2026
McNair Elementary School Renovation	Awaiting Board Approval	2026
Cross Oaks Elementary School Facility Upgrades	Awaiting Board Approval	2026
Crownover Middle School Facility Upgrades	Awaiting Board Approval	2026
Gallian Child Development Facility Upgrades	Awaiting Board Approval	2026
Providence Elementary School Facility Upgrades	Awaiting Board Approval	2026
Savannah Elementary School Facility Upgrades	Awaiting Board Approval	2026
Pecan Creek Elementary School Facility Upgrades	Awaiting Board Approval	2026
Paloma Creek Elementary School Marquee Upgrade	Awaiting Board Approval	2026
McMath Middle School Marquee Upgrade	Awaiting Board Approval	2026
New ATC	Planning & Design	TBD
Technology Office/Warehouse	Planning & Design	TBD



DENTON INDEPENDENT SCHOOL DISTRICT EMPOWERING LIFE-LONG LEARNERS

Construction, Planning & Growth

Borman Elementary School

November 2025

Borman Elementary School



2023 Bond Authorization
Architects – Corgan
Contractor – Joeris
Move In – TBD





Borman Elementary School



2023 Bond Authorization
Architects – Corgan
Contractor – Joeris
Move In – TBD

Tasks completed previous 90 days:

- Slabs on grade, slabs on deck & slabs on void to be completed
- ICF on A.B.C and D areas to be completed
- Steel erection to begin
- Roofing to begin in some areas
- Grackle Street construction to be completed

Upcoming Tasks:

- Complete roof deck, FRP roof, and roofing in multiple areas
- Begin exterior walls: waterproofing and masonry
- Build out inside rooms and install basic utilities
- Start interior finishes like tile, ceilings, and flooring
- Start interior framing, MEP rough-in, drywall, and early painting

Prepared by:





2023 Bond Authorization

Architects – Corgan

Contractor – Joeris

Move In – TBD







Borman Elementary School



2023 Bond Authorization
Architects – Corgan
Contractor – Joeris
Move In – TBD





DENTON INDEPENDENT SCHOOL DISTRICT EMPOWERING LIFE-LONG LEARNERS


Construction, Planning & Growth

Ryan High School

November 2025





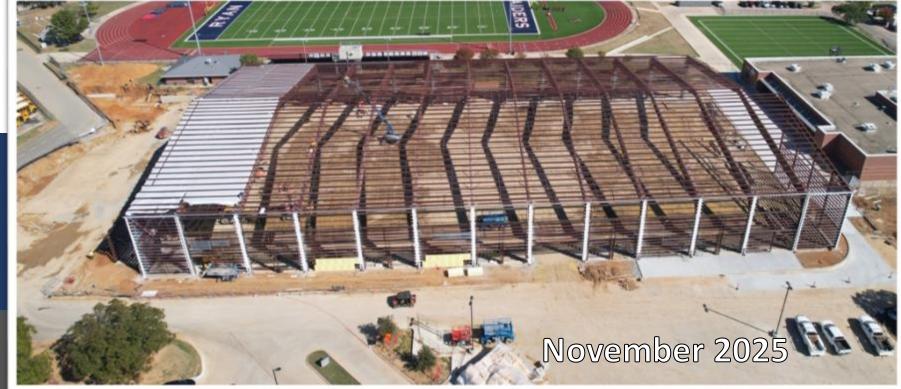



2023 Bond Authorization
Architects – VLK Architects
Contractor – Joeris
Move In – 2026

Tasks completed previous 90 days:

- Installed underground utilities for the building.
- Poured grade beams and retaining walls
- Poured Structural Slabs
- Erected the structural steel
- Started roof decking and wall sheathing

Upcoming tasks:

- Finish Roofing
- Sheathing, bricking, and metal panels on exterior walls
- Frame interior walls
- Interior MEP pathways
- Start Kalwall Panel install



















DENTON INDEPENDENT SCHOOL DISTRICT EMPOWERING LIFE-LONG LEARNERS

Construction, Planning & Growth

Transportation Center

November 2025









2023 Bond Authorization
Architects – VLK Architects
Contractor – Joeris
Move In – 2026

Tasks completed previous 90 days:

- Close in all exterior walls
- Frame all interior walls
- MEP rough-in in the office and shop areas
- Pouring site retaining walls

Upcoming tasks:

- Interior finishes
- Finish all MEP install
- Install new fueling system
- Site Paving

















DENTON INDEPENDENT SCHOOL DISTRICT EMPOWERING LIFE-LONG LEARNERS

Construction, Planning & Growth

Guyer High School

November 2025









2023 Bond Authorization
Architects – VLK Architects
Contractor – BWC
Move In – 2026

Tasks completed previous 90 days:

- Exterior Brick and Metal Panels
- Installed Kalwall Panels
- Interior Sheetrock, tape and bed
- MEP Installations
- Overhead doors

Upcoming tasks:

- Install turf
- Interior finishes
- Finish exterior site work
- Punch walks
- Clean up












Guyer High School Ag Barn



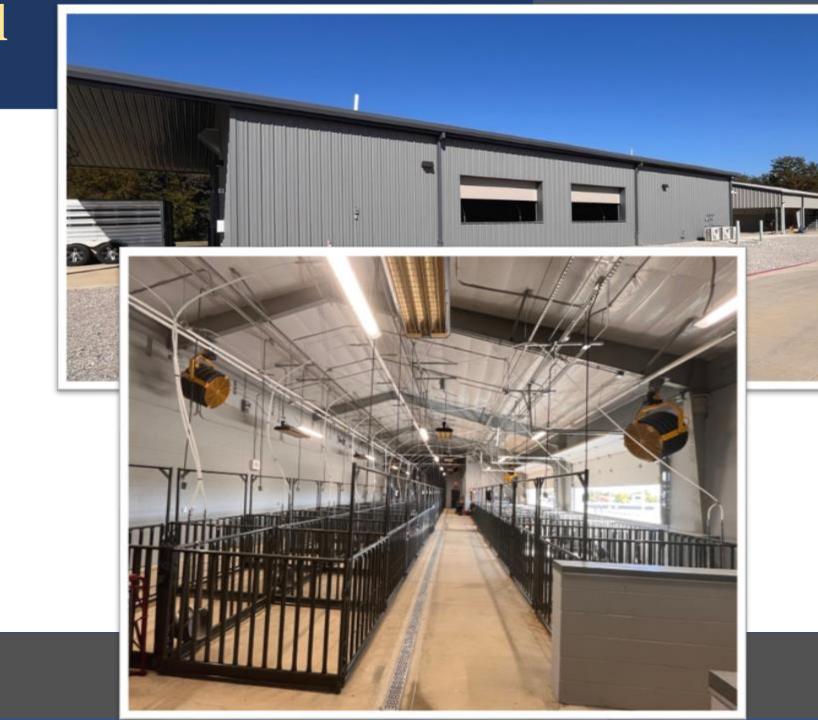

Guyer High School Concession











DENTON INDEPENDENT SCHOOL DISTRICT EMPOWERING LIFE-LONG LEARNERS

Construction, Planning & Growth

High School #5

November 2025

Denton High School #5







Denton High School #5







DENTON INDEPENDENT SCHOOL DISTRICT EMPOWERING LIFE-LONG LEARNERS

Construction, Planning & Growth

Ginnings Elementary School

November 2025

Ginnings Elementary School



2023 Bond Authorization
Architects – Corgan
Contractor – Balfour Beatty
Move In – TBD



Ginnings Elementary School



2023 Bond Authorization
Architects – Corgan
Contractor – Balfour Beatty
Move In – TBD





Questions?

Prepared by:

Brandon Boyter Executive Director of Construction, Planning & Growth
